



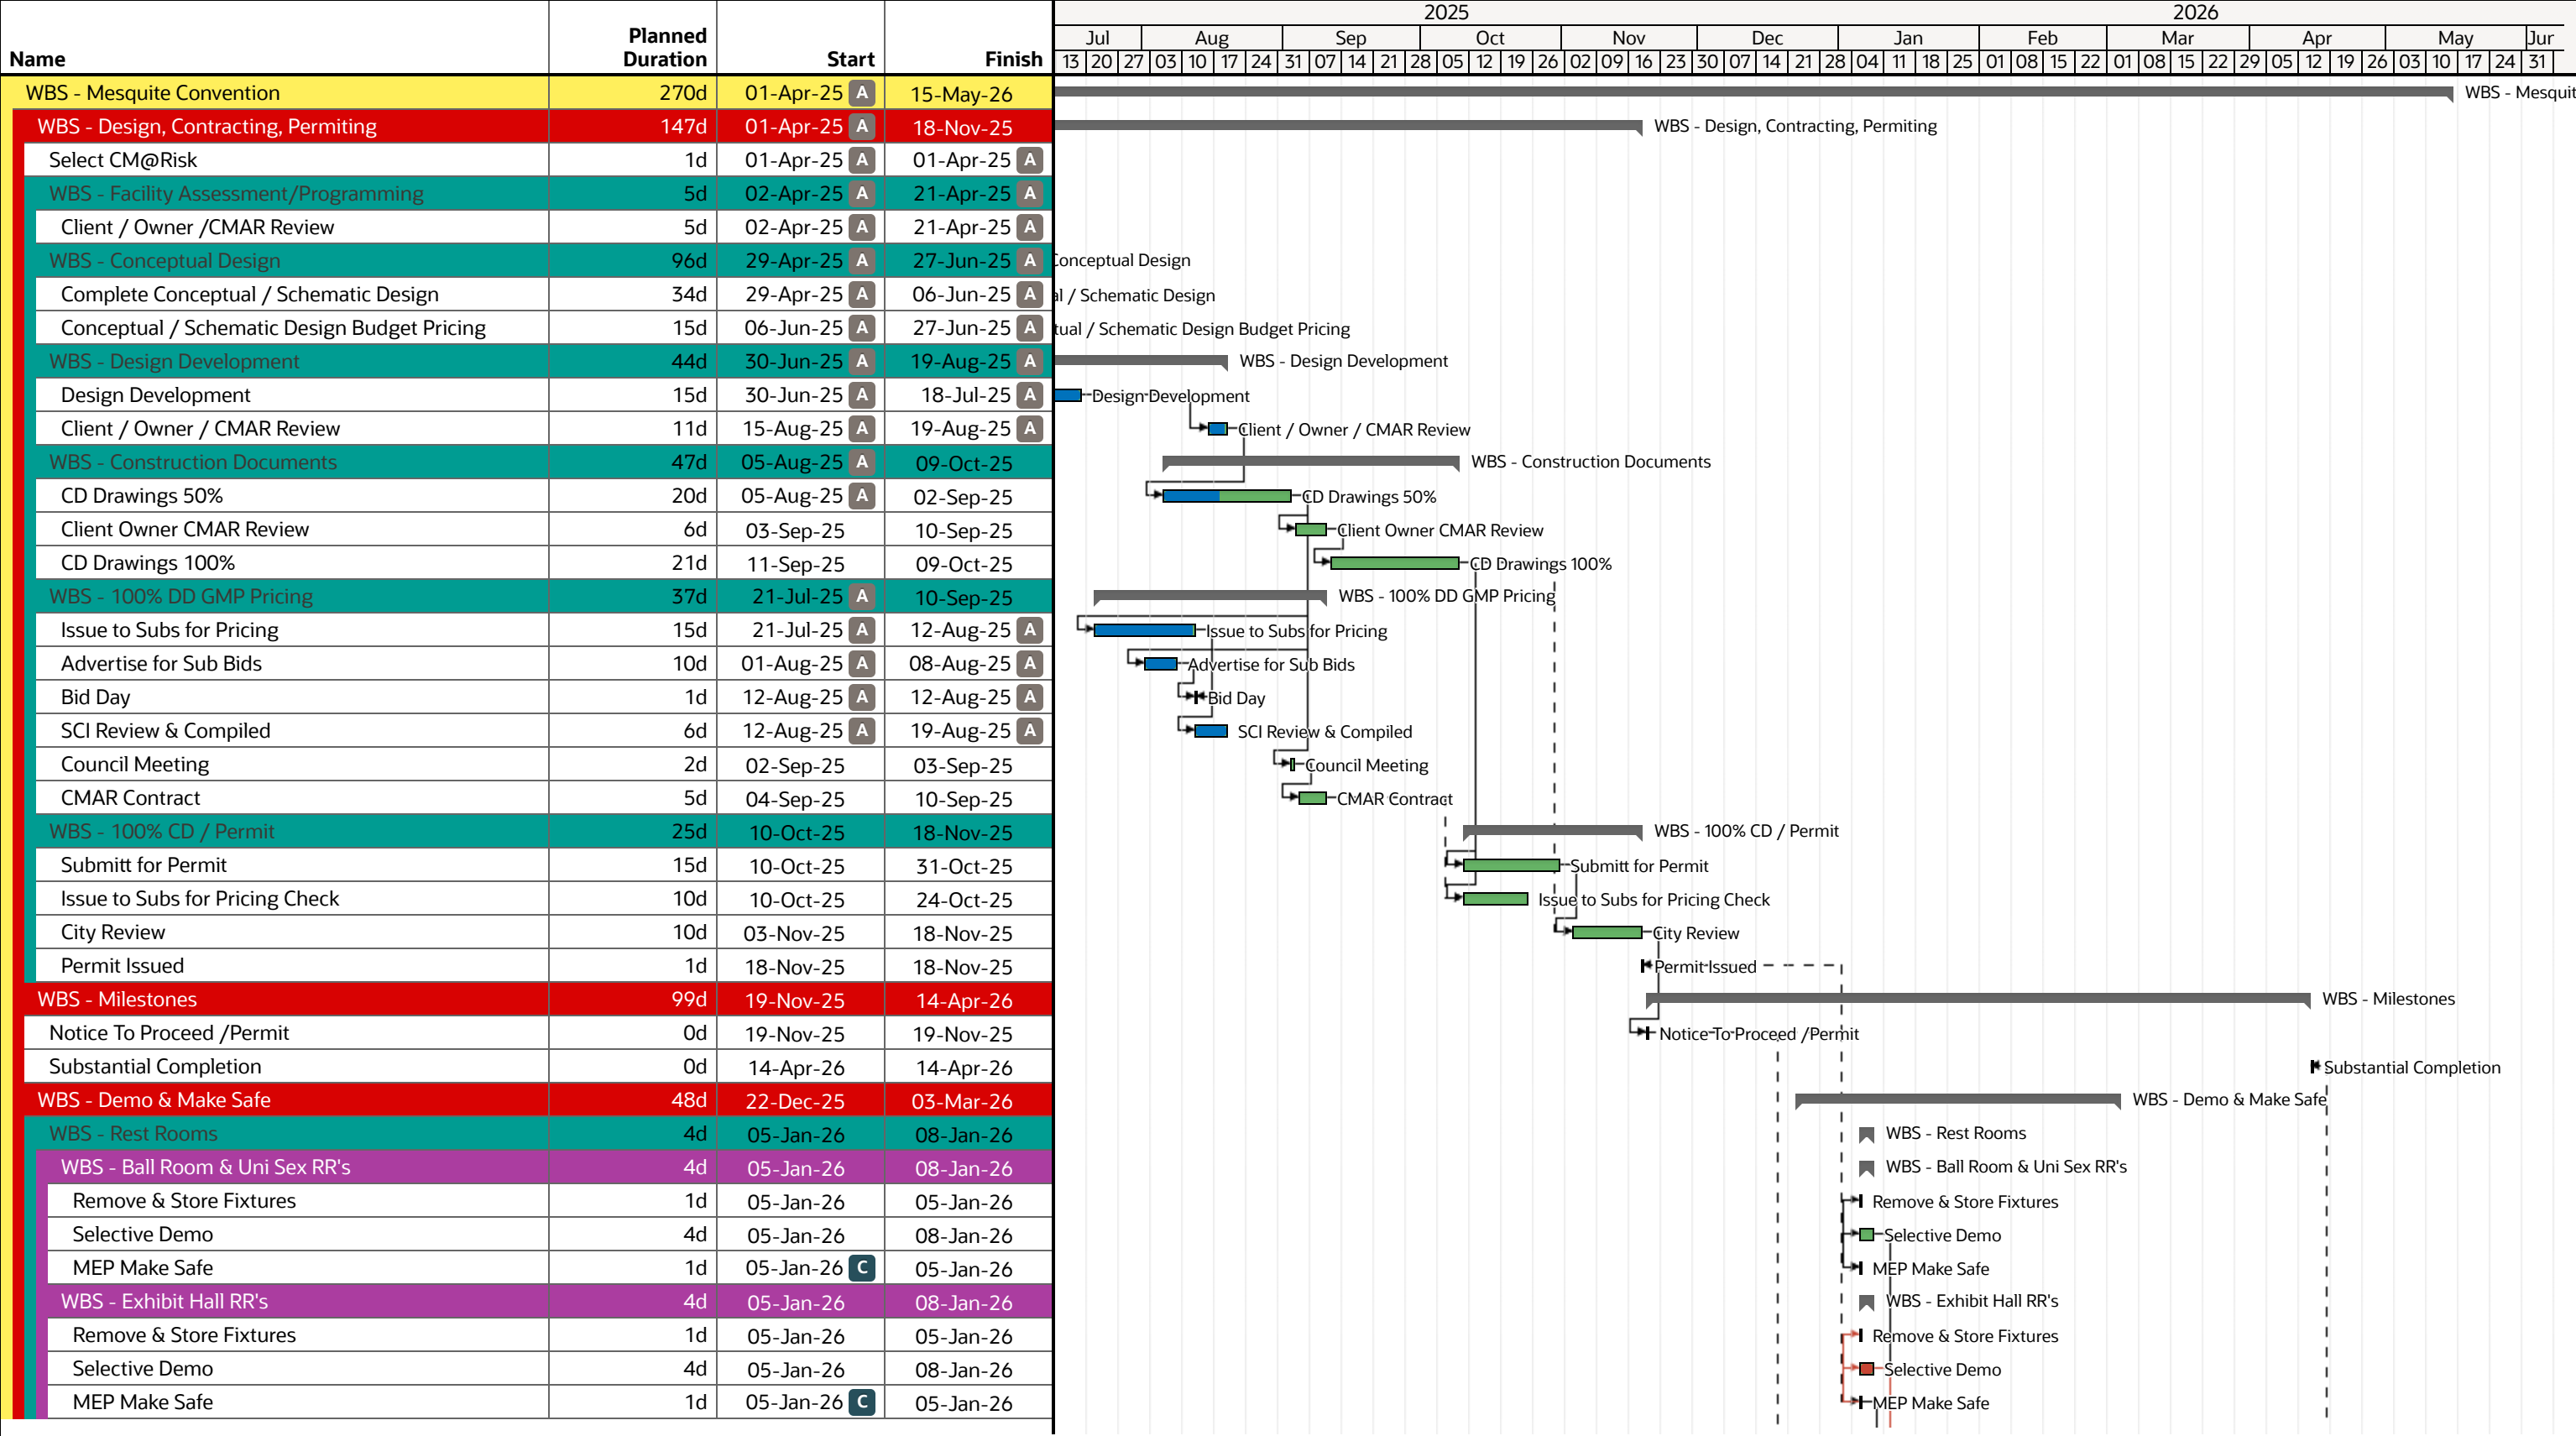

Name	Planned Duration	Start	Finish
WBS - Break Out Rooms	21d	22-Dec-25	22-Jan-26
WBS - Riata	6d	22-Dec-25	30-Dec-25
Electrical Make Safe	1d	22-Dec-25 C	22-Dec-25
Remove Wall Paper	5d	23-Dec-25	30-Dec-25
Remove Carpet	2d	23-Dec-25	24-Dec-25
WBS - Latigo	11d	22-Dec-25	07-Jan-26
Electrical Make Safe	1d	22-Dec-25	22-Dec-25
Remove Carpet	2d	26-Dec-25	29-Dec-25
Remove Wall Paper	5d	31-Dec-25	07-Jan-26
WBS - Pelham	16d	22-Dec-25	14-Jan-26
Electrical Make Safe	1d	22-Dec-25	22-Dec-25
Remove Carpet	2d	30-Dec-25	31-Dec-25
Remove Wall Paper	5d	08-Jan-26	14-Jan-26
WBS - Cayuse	21d	22-Dec-25	22-Jan-26
Electrical Make Safe	1d	22-Dec-25	22-Dec-25
Remove Carpet	2d	02-Jan-26	05-Jan-26
Remove Wall Paper	5d	15-Jan-26	22-Jan-26
WBS - Ballroom	25d	09-Jan-26	13-Feb-26
WBS - Salon A	5d	09-Jan-26	15-Jan-26
Remove Wall Paper	5d	09-Jan-26	15-Jan-26
Remove Carpet	3d	09-Jan-26	13-Jan-26
MEP Make Safe	1d	09-Jan-26	09-Jan-26
WBS - Salon B	9d	12-Jan-26	23-Jan-26
MEP Make Safe	1d	12-Jan-26	12-Jan-26
Remove Carpet	3d	14-Jan-26	16-Jan-26
Remove Wall Paper	5d	16-Jan-26	23-Jan-26
WBS - Salon C	13d	13-Jan-26	30-Jan-26
MEP Make Safe	1d	13-Jan-26	13-Jan-26
Remove Carpet	2d	20-Jan-26	21-Jan-26
Remove Wall Paper	5d	26-Jan-26	30-Jan-26
WBS - Salon D	17d	14-Jan-26	06-Feb-26
MEP Make Safe	1d	14-Jan-26	14-Jan-26
Remove Carpet	2d	22-Jan-26	23-Jan-26
Remove Wall Paper	5d	02-Feb-26	06-Feb-26
WBS - Salon E	21d	15-Jan-26	13-Feb-26
MEP Make Safe	1d	15-Jan-26	15-Jan-26
Remove Carpet	2d	26-Jan-26	27-Jan-26
Remove Wall Paper	5d	09-Feb-26	13-Feb-26
WBS - Pre Function	10d	06-Jan-26	20-Jan-26
WBS - Exhibit Hall Pre Function	9d	07-Jan-26	20-Jan-26

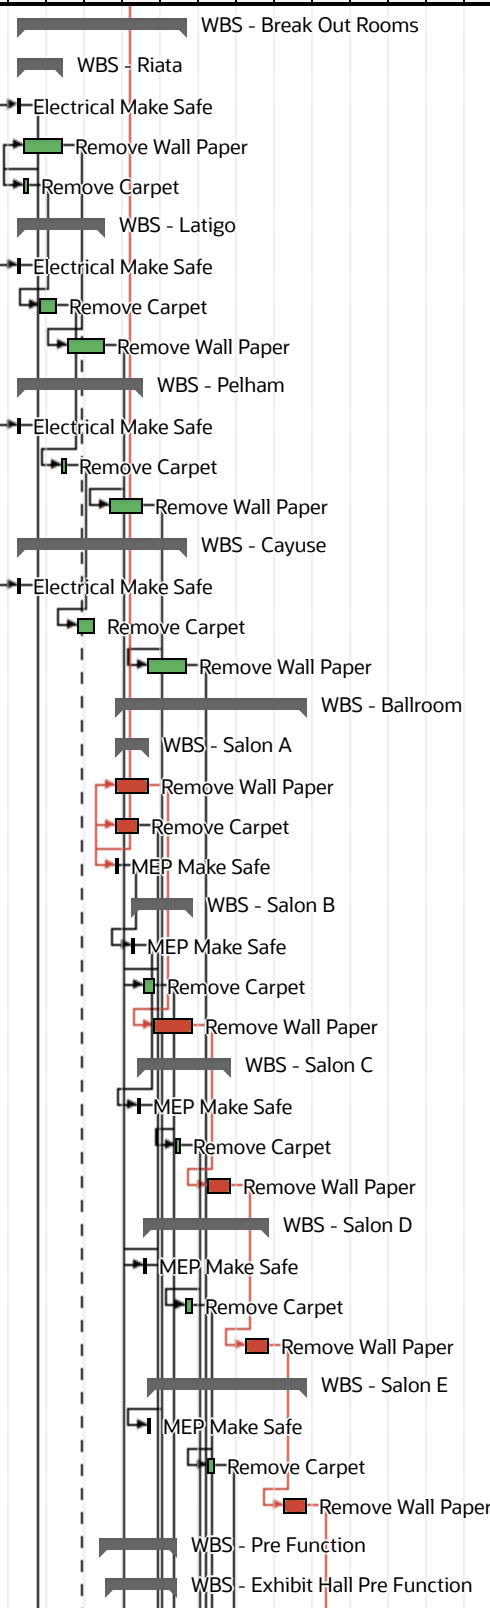

 Current
  Progress
  Critical
  Milestones
  Summary

[illegible]

Current
 Progress
 Critical
 Milestones
 Summary

[illegible]

 Current
  Milestones

 Progress
  Summary

 Critical

